Project Updates



Town of Beaufort January 25, 2021

13 Active Projects

- 2 Parks & Recreation
 - \rightarrow 1 Makeovers
 - \rightarrow 1 New
- 4 Street and Pedestrian Improvements
- 5 Utility
 - \rightarrow 1 Water
 - \rightarrow 2 Sewer
 - \rightarrow 1 Water & Sewer
 - ightarrow 1 Water, Sewer, and Stormwater
- 1 Stormwater
- 1 Building

(1 through 7)

- Cedar Street Park
- Topsail Park
- FY20 Street Rehabilitation & Construction
- Turner Street 100 Block Pedestrian Improvements
- Town Wide Sidewalks (Part 5-FY20 Street Rehabilitation & Construction)
- Cedar Street Water & Sewer Rehabilitation & Replacements
- Campen Road Waterline Extension/Upgrade

(1 through 7)

- Cedar Street Park
- Topsail Park
- FY20 Street Rehabilitation & Construction
- Turner Street 100 Block Pedestrian Improvements
- Town Wide Sidewalks (Part 5-FY20 Street Rehabilitation & Construction)
- Cedar Street Water & Sewer Rehabilitation & Replacements
- Campen Road Waterline Extension/Upgrade

Topsail Park





- Awaiting Plants
- 2 to 3 Week Completion









- ✓ Stanton Road
- ✓ Hedrick Street
- ✓ Mashburn Avenue
- ✓ Professional Park Drive
- ✓ Jefferson Street
- ✓ Eastern Avenue
- ✓ Ricks Avenue
- ✓ Sherwood Boulevard
- ✓ Live Oak Street 100 Block
- ✓ Gordon Street
- ✓ Laurel Lane
- ✓ Safrit Drive
- ✓ Craven Avenue
- ✓ Carteret Avenue
- ✓ Pollock Street
- ✓ Olivia Road

- ✓ Live Oak Street 300 Block
- Taylors Creek Road
- Campen Road





Concrete Work

- ✓ Replace 467 feet of rolled curb
- Replace 82 feet of curb & gutter
- Replace 69 sq. yards of sidewalk
- Replace **16 each** concrete curb ramps

Pavement Markings

- 75 feet of 4" wide white lines
- 1,078 feet of 4" wide yellow lines
- 387 feet of 24" wide crosswalk lines

Seal Coating

• Marsh Street, Broad to Mulberry

Jan 25th - thru Feb 12th

Week of Jan 25th

New Street Construction

✓ Howard Jr. Lane



Orange Street

- Remaining Work
 - Complete storm sewer
 - Test & disinfect water line
 - Switchover water services
 - "Test" gravity sewer



Orange Street


- Remaining Work
 - Complete storm sewer
 - Test & disinfect water line
 - Switchover water services
 - "Test" gravity sewer
 - Reconstruct street base
 - Construct permeable concrete parking lane
 - Place asphalt surface
- February 12th projected completion




Turner Street 100 Block Street Improvements (West Side)

- Work Underway
 - Week of Jan 11th \rightarrow Demolition
 - Week of Jan 18th \rightarrow Duke Energy
 - Next \rightarrow Relocate Water Service Lines
- Expanded Project
 - Approved Oct 12, 2020
 - Negotiating Change Orders




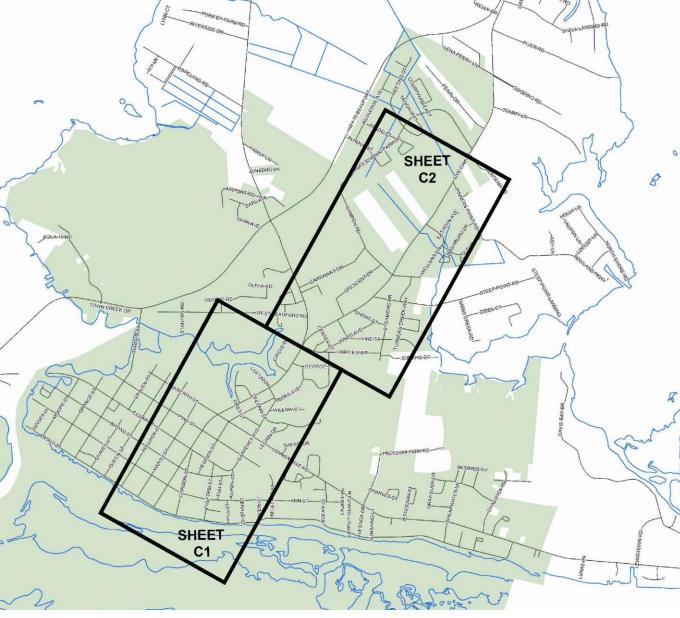

Town Wide Sidewalks

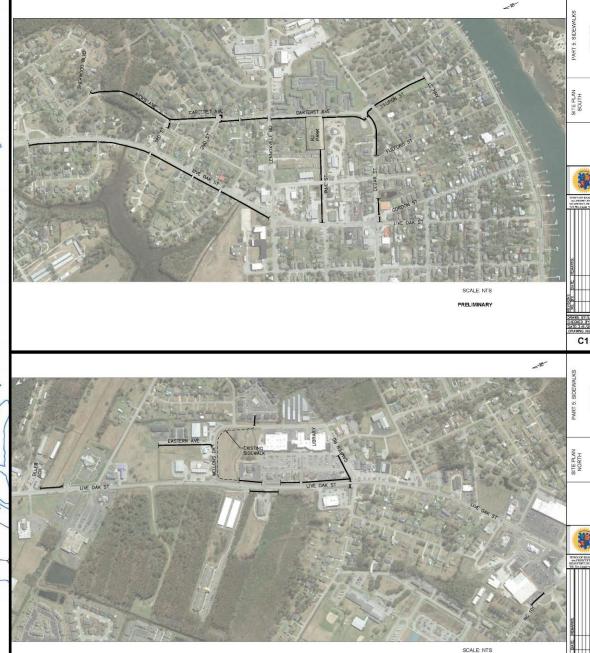

C2

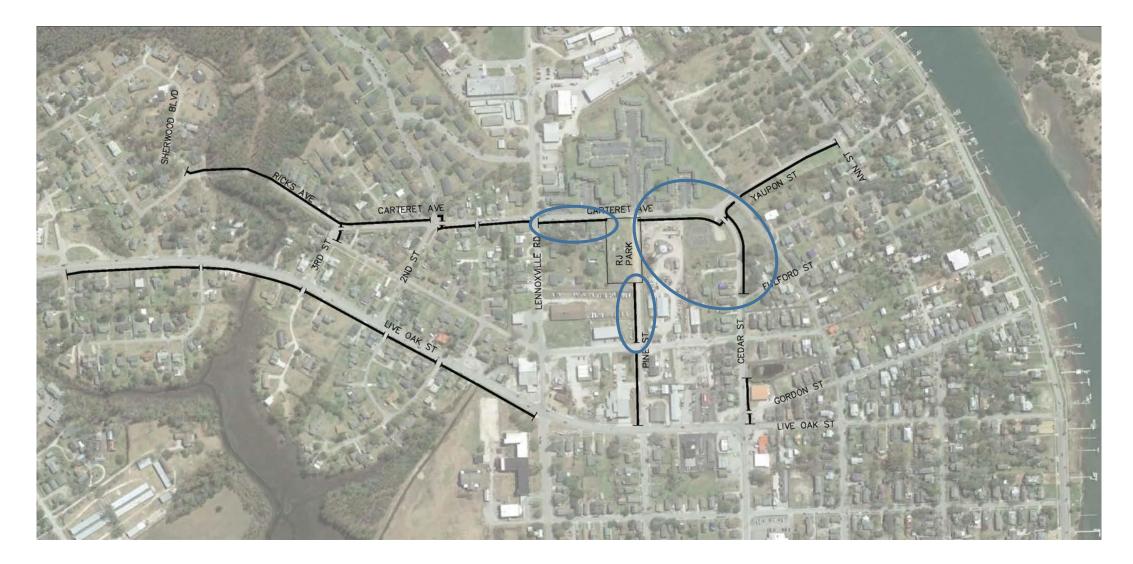

Town Wide Sidewalks

- Near-park segments first
- March 29th start (tentative)







Cedar Street Utility Rehabilitation & Replacements

- Work Underway
 - January 11th construction start
- May 3rd Completion (Schedule)
 - ≈ 1 week behind

(8 through 13)

- USDA Funding Applications (Water, Sewer & Stormwater)
- Wastewater Asset Inventory Assessment
- High-Rate Infiltration System Permit Requisition
- Electric Vehicle Charging
- Meeting Street Drainage Improvements
- Town Hall Reception Area Renovation

(8 through 13)

- USDA Funding Applications (Water, Sewer & Stormwater)
- Wastewater Asset Inventory Assessment
- High-Rate Infiltration System Permit Requisition
- Electric Vehicle Charging Station
- Meeting Street Drainage Improvements
- Town Hall Reception Area Renovation

USDA Funding Applications (Water, Sewer & Stormwater)

Project Estimates:

Water...... \$ 8.25 million Sewer...... \$11.70 million Stormwater... <u>\$ 8.03 million</u> **\$27.98 million**


Proposed USDA loan/grant offer expected – January 25th goal missed



Electric Vehicle Charging

Potential Funding

- Phase 1 Zero Emission Vehicle (ZEV) Infrastructure Program
- Application filed January 25th
 -\$10,000 grant towards \$24,800 cost

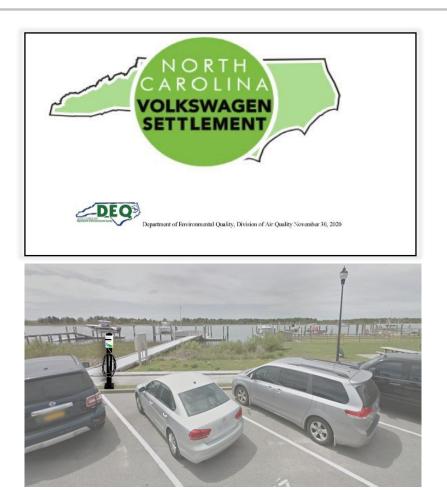





Town Hall Reception Area Renovation

Construction by Public Works Staff

- Awaiting Transaction Windows
- Carpet & Clean-up
- Furniture Delivery
 - Week of February 1st

Town Hall Steps, ADA Ramp & Sidewalks

Projected Completion

January 29th
 (Pending Handrail Delivery)



Project Updates



QUESTIONS?

COMMENTS?
