

Project Updates



Town of Beaufort

January 25, 2021

Active Projects

13 Active Projects

- 2 Parks & Recreation
 - 1 Makeovers
 - 1 New
- 4 Street and Pedestrian Improvements
- 5 Utility
 - 1 Water
 - 2 Sewer
 - 1 Water & Sewer
 - 1 Water, Sewer, and Stormwater
- 1 Stormwater
- 1 Building



Active Projects

(1 through 7)

- Cedar Street Park
 - Topsail Park
 - FY20 Street Rehabilitation & Construction
 - Turner Street 100 Block Pedestrian Improvements
 - Town Wide Sidewalks (Part 5-FY20 Street Rehabilitation & Construction)
 - Cedar Street Water & Sewer Rehabilitation & Replacements
 - Campen Road Waterline Extension/Upgrade
-





Active Projects

(1 through 7)

- Cedar Street Park
 - Topsail Park
 - FY20 Street Rehabilitation & Construction
 - Turner Street 100 Block Pedestrian Improvements
 - Town Wide Sidewalks (Part 5-FY20 Street Rehabilitation & Construction)
 - Cedar Street Water & Sewer Rehabilitation & Replacements
 - Campen Road Waterline Extension/Upgrade
-

Topsail Park

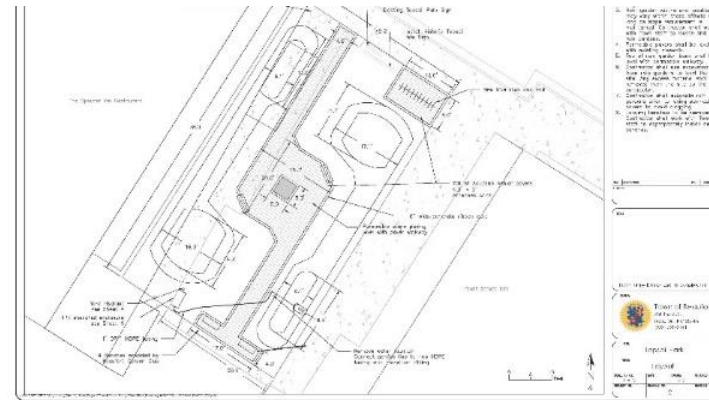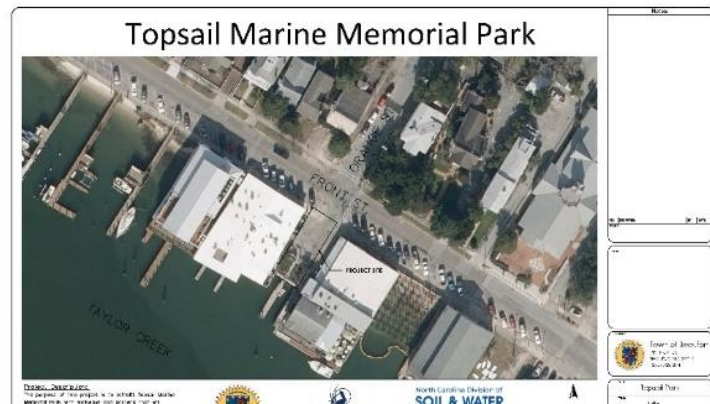

- Awaiting Plants
- 2 to 3 Week Completion

FY20 Street Rehabilitation and Construction

- ✓ Stanton Road
- ✓ Hedrick Street
- ✓ Mashburn Avenue
- ✓ Professional Park Drive
- ✓ Jefferson Street
- ✓ Eastern Avenue
- ✓ Ricks Avenue
- ✓ Sherwood Boulevard
- ✓ Live Oak Street 100 Block
- ✓ Gordon Street
- ✓ Laurel Lane
- ✓ Safrit Drive
- ✓ Craven Avenue
- ✓ Carteret Avenue
- ✓ Pollock Street
- ✓ Olivia Road
- ✓ Live Oak Street 300 Block
- ✓ Taylors Creek Road
- ✓ Campen Road





FY20 Street Rehabilitation and Construction

Concrete Work

- ✓ Replace 467 feet of rolled curb
- Replace 82 feet of curb & gutter
- Replace 69 sq. yards of sidewalk
- Replace 16 each concrete curb ramps

Jan 25th
thru
Feb 12th

Pavement Markings

- 75 feet of 4" wide white lines
- 1,078 feet of 4" wide yellow lines
- 387 feet of 24" wide crosswalk lines

Week of Jan
25th

Seal Coating

- Marsh Street, Broad to Mulberry

FY20 Street Rehabilitation and Construction

New Street Construction

✓ Howard Jr. Lane

- Souza Development Access Street
 - Paused
 - Stormwater Permitting



FY20 Street Rehabilitation and Construction

Orange Street

- Remaining Work
 - Complete storm sewer
 - Test & disinfect water line
 - Switchover water services
 - “Test” gravity sewer



FY20 Street Rehabilitation and Construction

Orange Street


- Remaining Work
 - Complete storm sewer
 - Test & disinfect water line
 - Switchover water services
 - “Test” gravity sewer
 - Reconstruct street base
 - Construct permeable concrete parking lane
 - Place asphalt surface
- February 12th projected completion





Turner Street 100 Block Street Improvements (West Side)

- Work Underway
 - Week of Jan 11th → Demolition
 - Week of Jan 18th → Duke Energy
 - Next → Relocate Water Service Lines
- Expanded Project
 - Approved Oct 12, 2020
 - Negotiating Change Orders



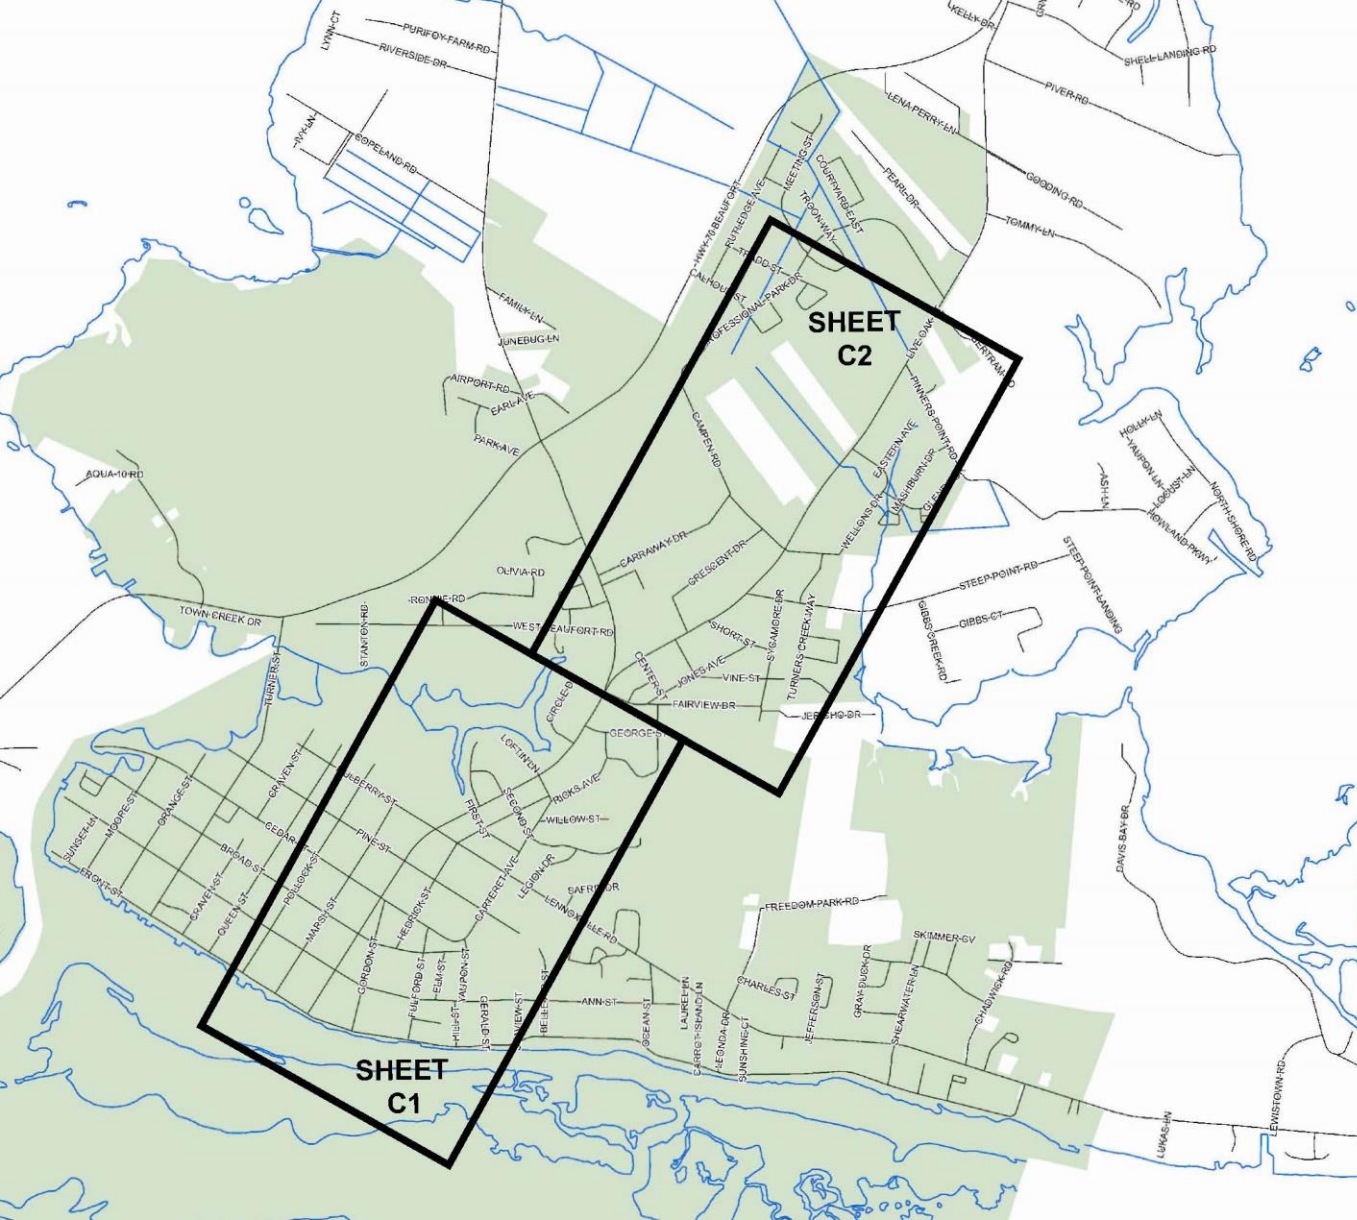

Town Wide Sidewalks

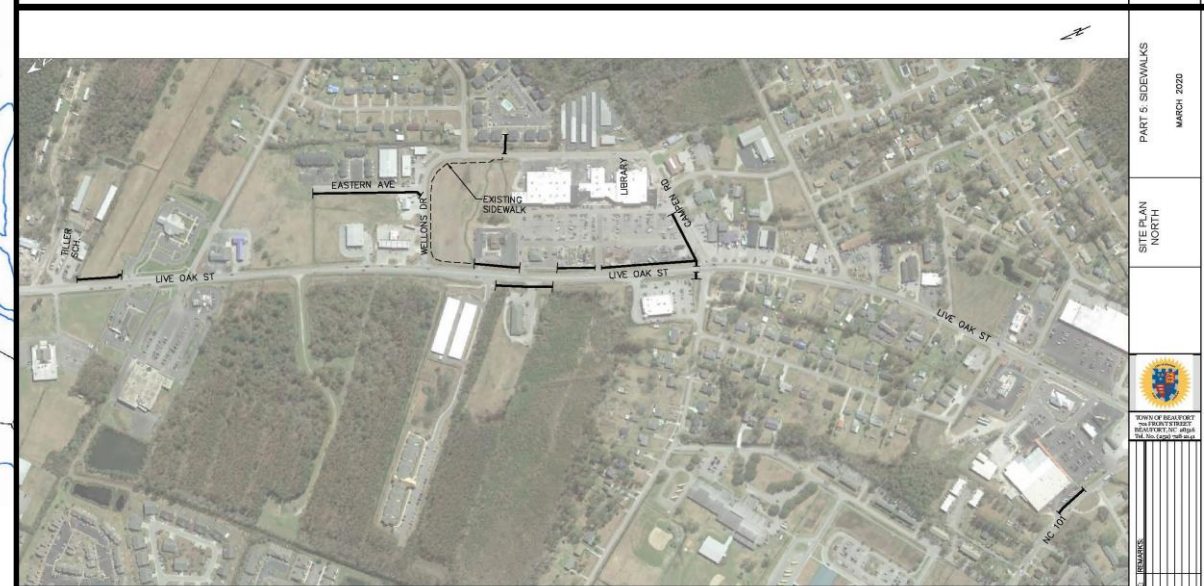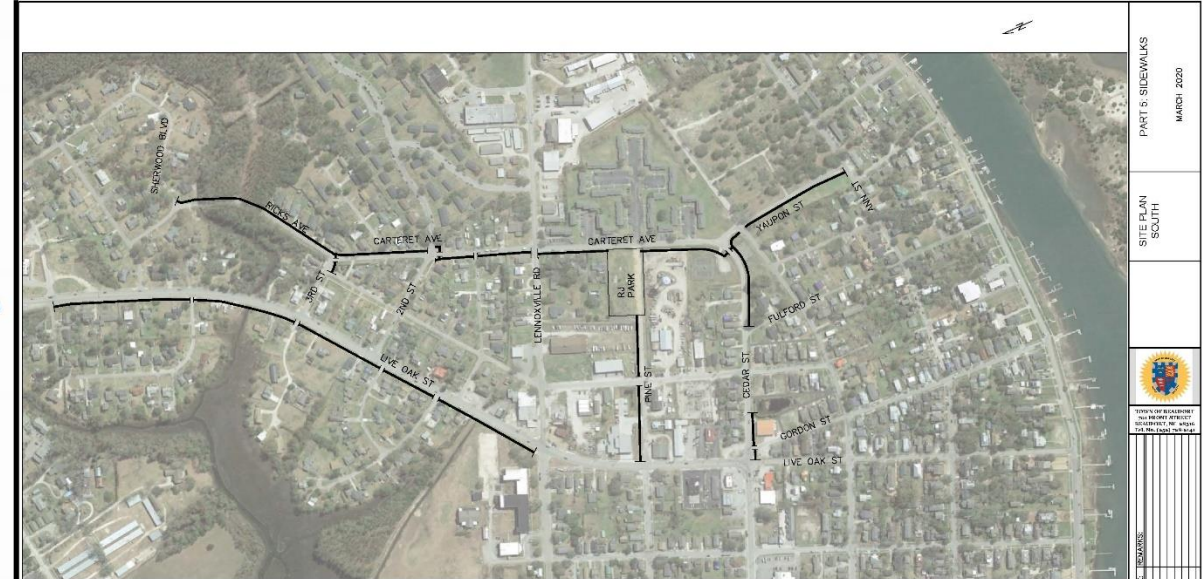



Town Wide Sidewalks

- Near-park segments first
- March 29th start (tentative)



Cedar Street Utility Rehabilitation & Replacements

- Work Underway
 - January 11th construction start
- May 3rd Completion (Schedule)
 - $\approx$ 1 week behind



Active Projects

(8 through 13)

- USDA Funding Applications (Water, Sewer & Stormwater)
 - Wastewater Asset Inventory Assessment
 - High-Rate Infiltration System Permit Requisition
 - Electric Vehicle Charging
 - Meeting Street Drainage Improvements
 - Town Hall Reception Area Renovation
-

Active Projects

(8 through 13)

- USDA Funding Applications (Water, Sewer & Stormwater)
- Wastewater Asset Inventory Assessment
- High-Rate Infiltration System Permit Requisition
- Electric Vehicle Charging Station
- Meeting Street Drainage Improvements
- Town Hall Reception Area Renovation

USDA Funding Applications (Water, Sewer & Stormwater)

Project Estimates:

Water.....	\$ 8.25 million
Sewer.....	\$11.70 million
Stormwater...	<u>\$ 8.03 million</u>
	\$27.98 million

Proposed USDA loan/grant offer expected



– January 25th goal missed



Electric Vehicle Charging

Potential Funding

- Phase 1 Zero Emission Vehicle (ZEV) Infrastructure Program
- Application filed January 25th
 - \$10,000 grant towards \$24,800 cost

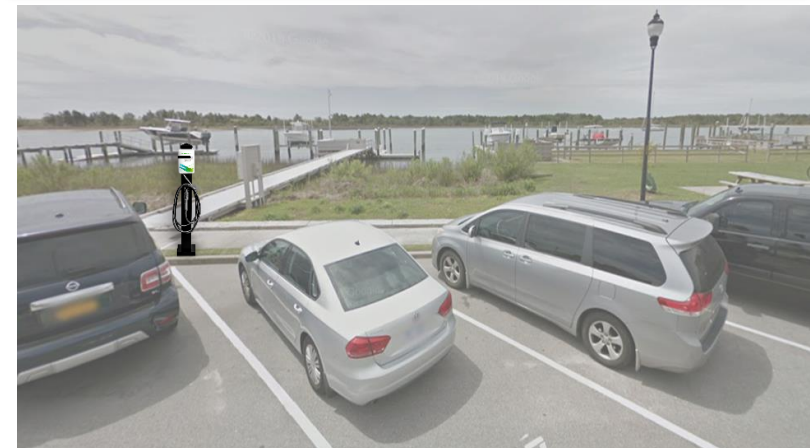



Town Hall Reception Area Renovation

Construction by Public Works Staff

- Awaiting Transaction Windows
- Carpet & Clean-up
- Furniture Delivery
- Week of February 1st

Town Hall

Steps, ADA Ramp & Sidewalks

Projected Completion
— January 29th
(Pending Handrail Delivery)



Project Updates



QUESTIONS?



COMMENTS?
